CORPORATE TECHNOLOGY

ENTERPRISE TECHNOLOGY SOLUTIONS

Planview – Jira Integration Overview: Work Traceability and Agile Costing



Nationwide®
is on your side

Two integrations exist between Planview E1 and Jira: Work Traceability and Agile Costing

Work Traceability

Work items in Planview E1 are connected to user stories in Jira by syncing Epics across the tools

Status is reported back to Planview E1 on work completed and still remaining






Timesheets created automatically for Whoville teams using work in progress tracked in Jira

Agile Costing


Work Traceability: Why integrate? Nationwide is moving to an end to end delivery focused workflow…

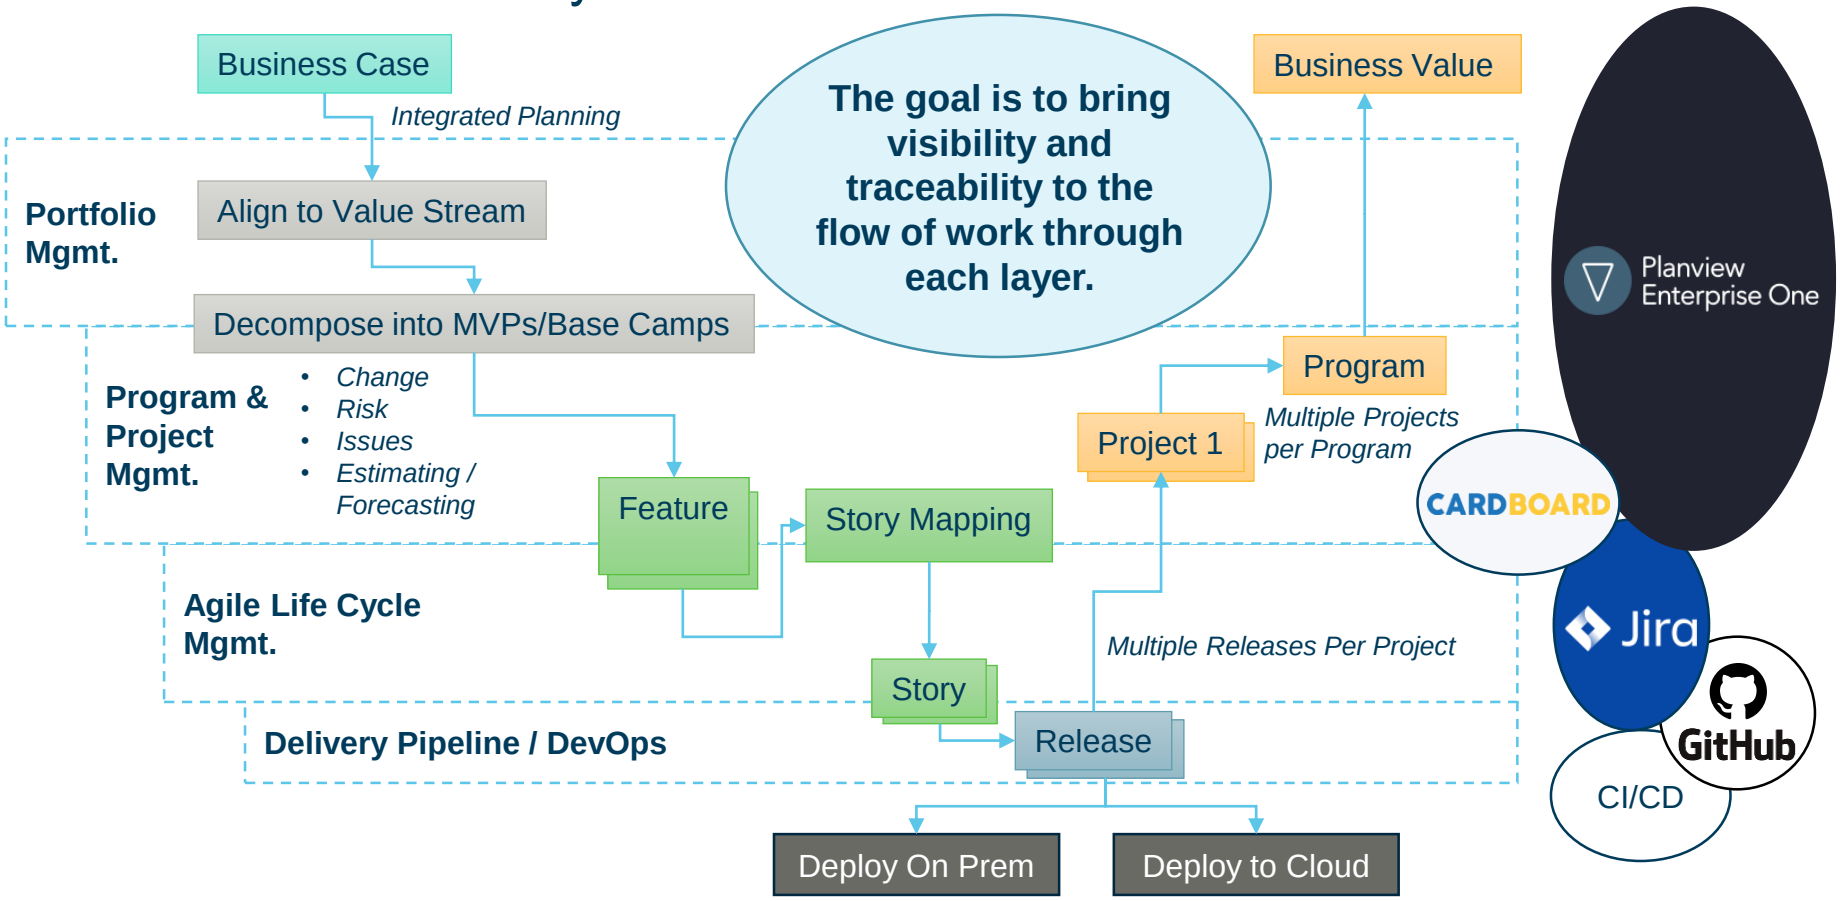

Benefits

- Increased visibility of work in progress to Portfolio, Program and Project management levels
- More transparency of work priority to and across lines
- Allows each level to work in their tool of choice without duplicated status or entry efforts


Work Traceability: Integration overview

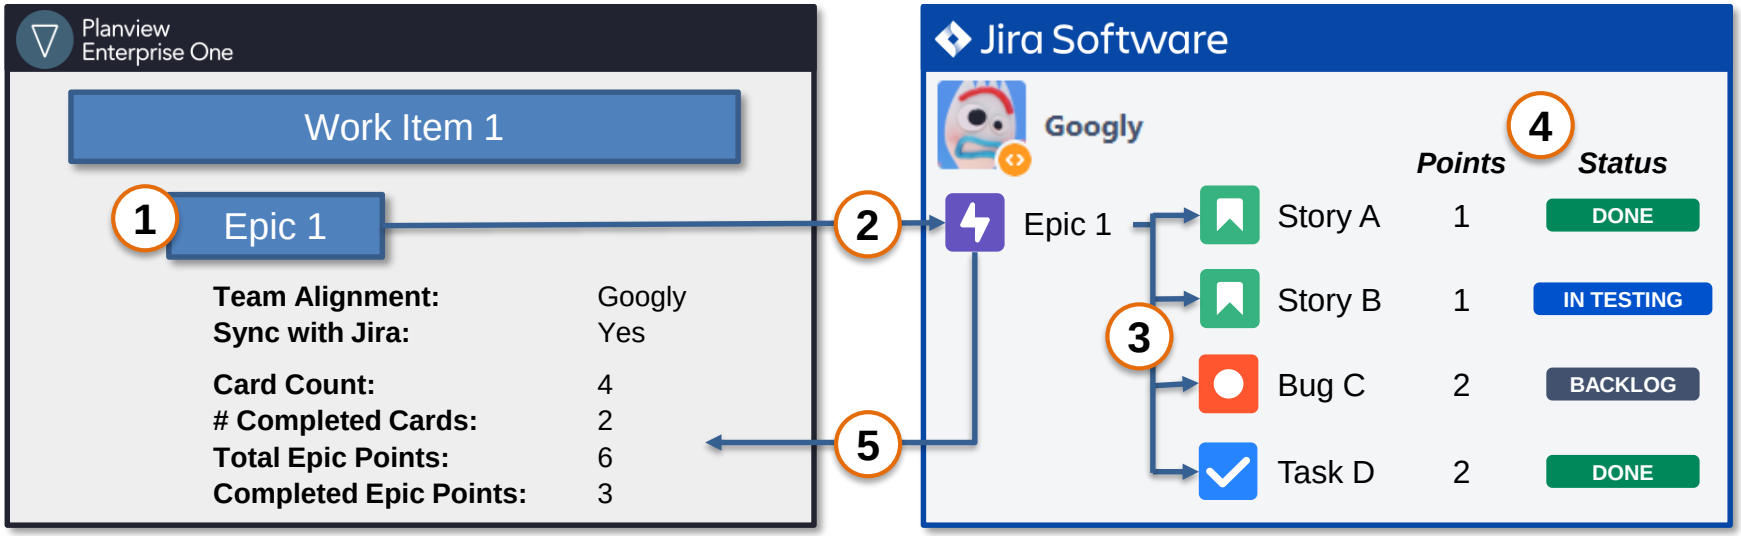


1. Epic is created in a Work Item's Work Breakdown Structure (WBS). The following fields must be specified:
   - **Team alignment (Jira project):** Googly
   - **Sync with Jira:** Yes
2. Epic is created in the specified Jira project and kept in sync with E1 (every 5 min)
3. Story, Bug, and Task issues are linked to the created epic using the Epic Link field
4. As story point values are defined, and issues are transitioned through statuses, the Epic in Jira will be updated with a summary of points and issue count
5. The following fields are synced to the Epic in E1:
   - **Card Count**
   - **Number Completed Cards**
   - **Total Epic Points**
   - **Total Completed Epic Points**

Work Traceability: Planview E1 Work Item templates define the WBS level for Epics


Option 1 - Level 7 Template

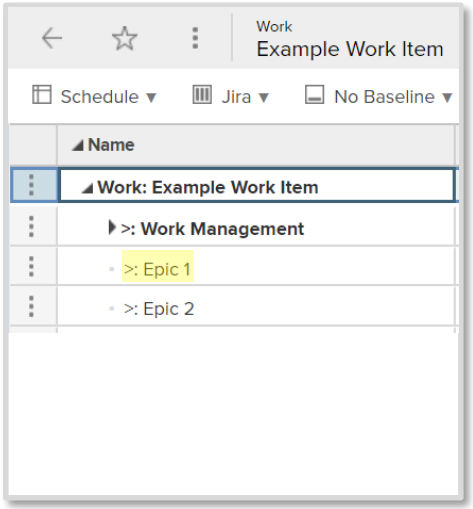

Option 2 - Level 8 Template

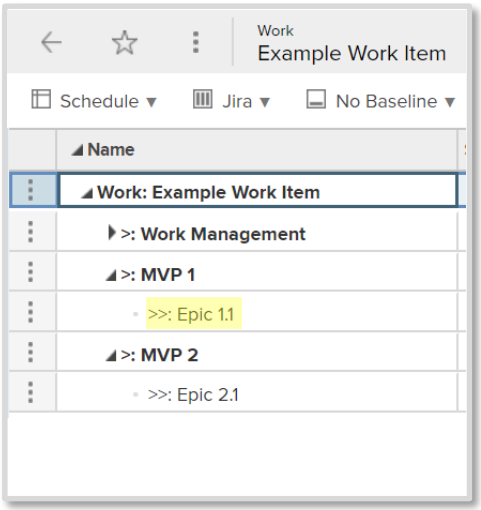


Option 3 - Level 9 Template

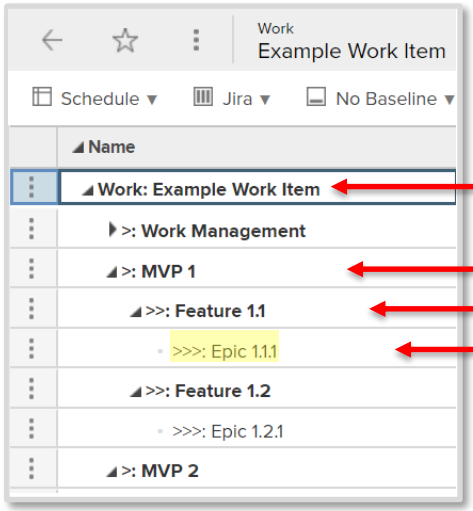


- Planview E1 will be used for many types of work with different decomposition needs:
  - Tier 1 programs vs. run support
- Templates allow work owners to choose how many levels of work decomposition are needed
- The template level defines which level of the WBS will sync with Jira
- Levels are indicated by arrows: **>** Level 7 **>>** Level 8 **>>>** Level 9

Work Traceability: Work item managers are prompted to select a template when creating their work items

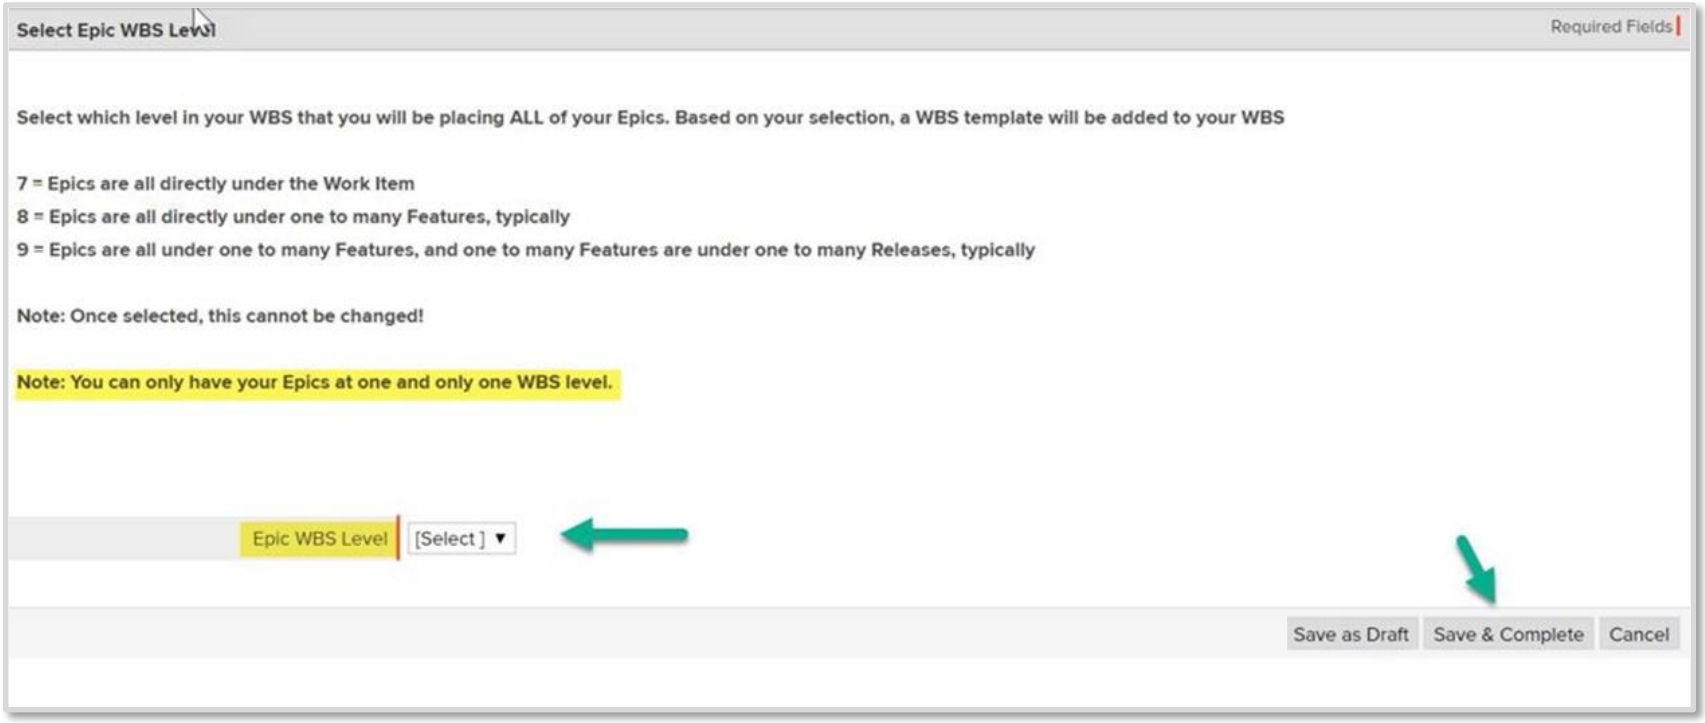


Work Traceability: Fields included in Epic Sync

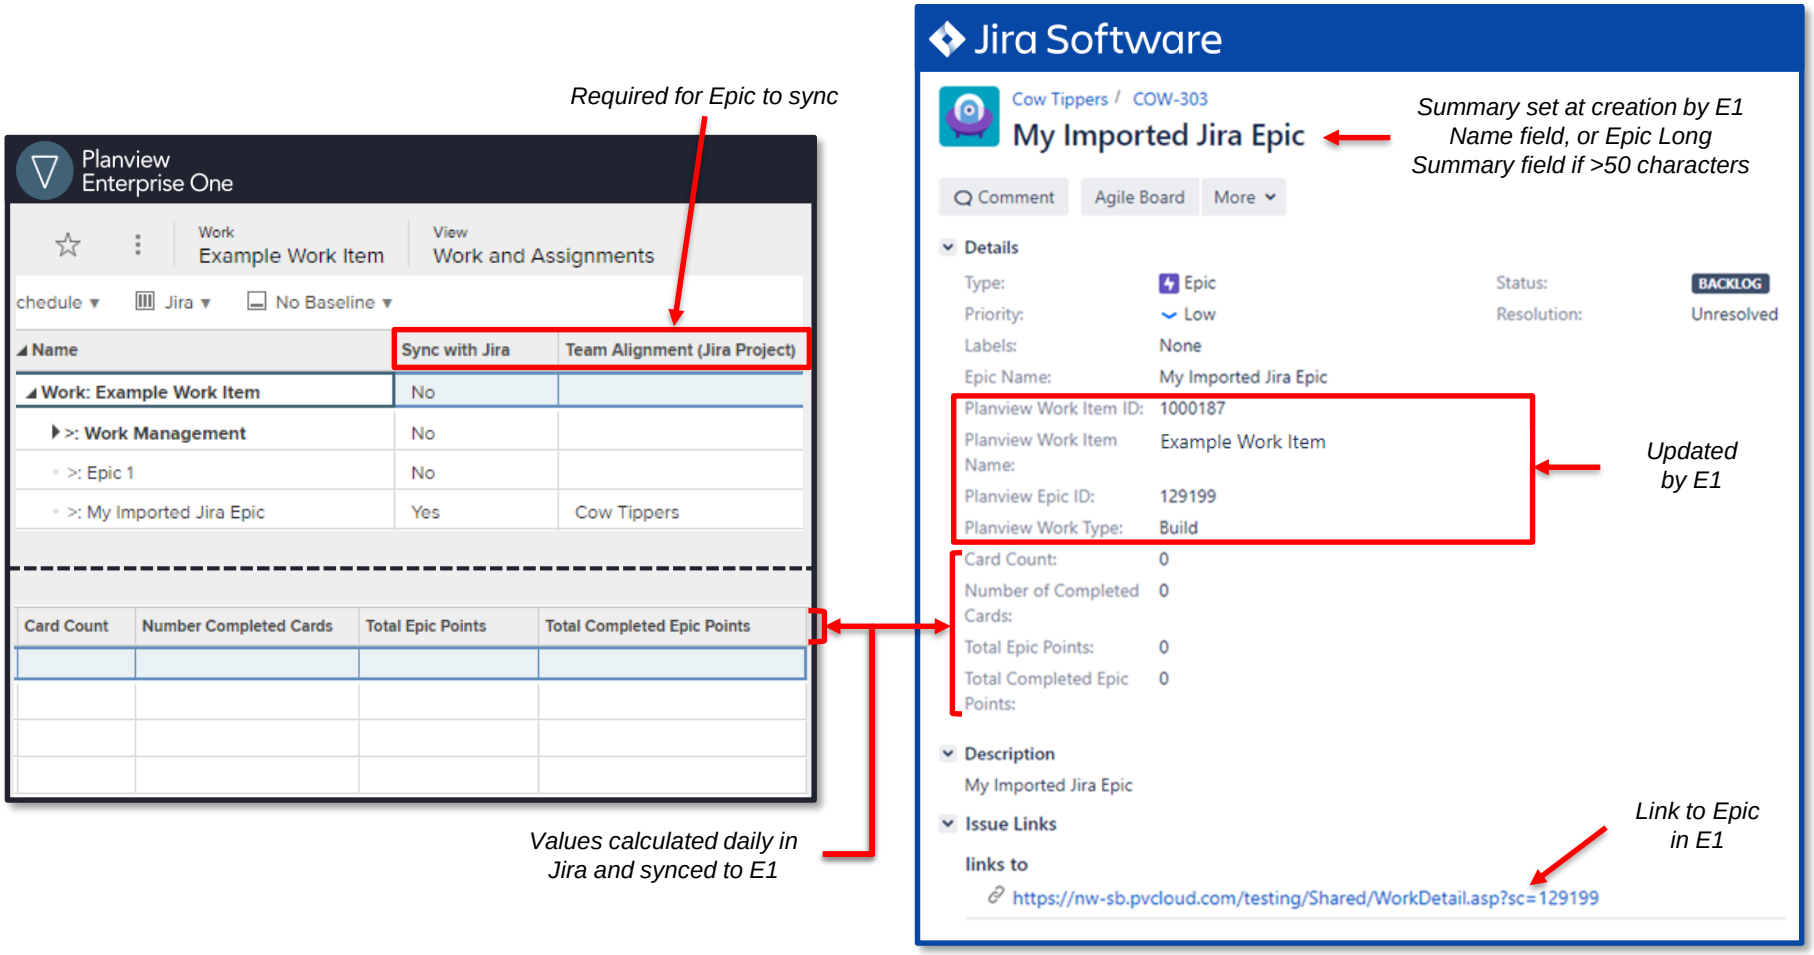


Work Traceability: Epics will sometimes span multiple teams – In these cases there are two options:

Option 1: Epics generated from E1 land in an owning team's workspace

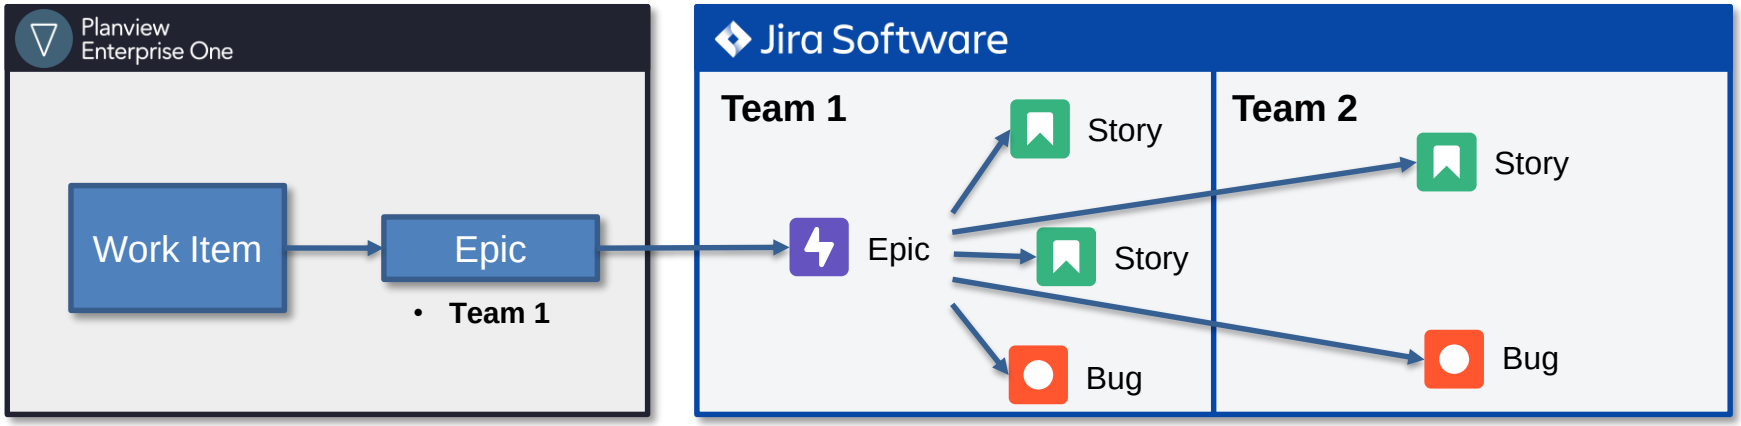

Option 2: Epics generated from E1 land in an "off the line" workspace

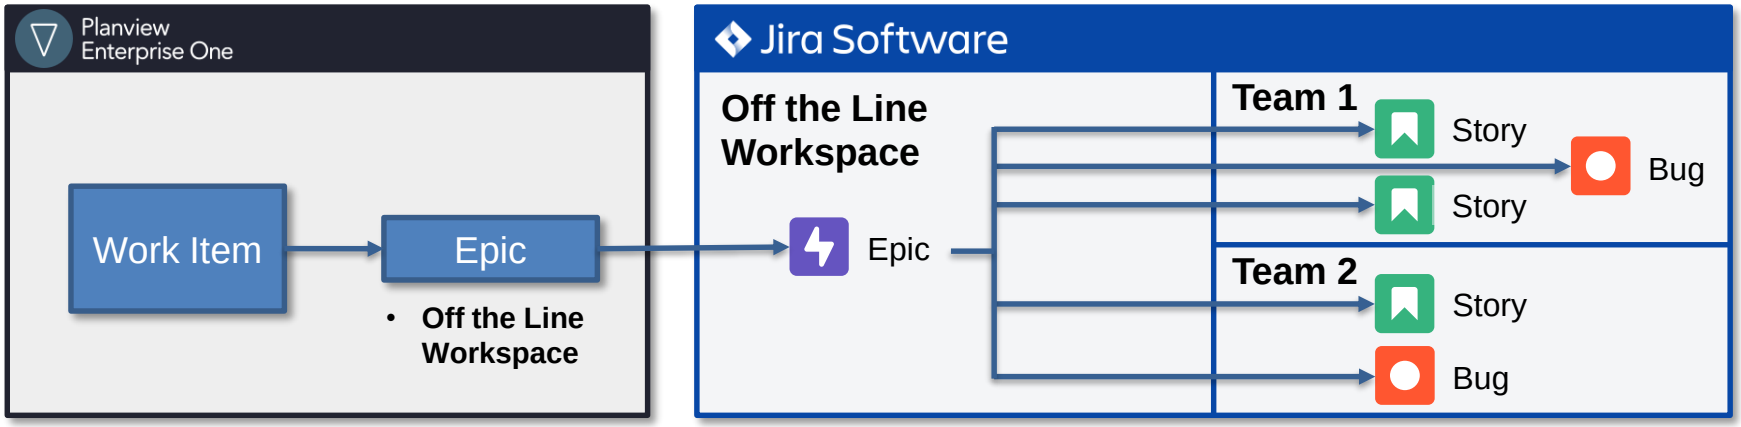

Work Traceability: Helpful tidbits

- Epics created in Jira will not sync to E1
  - If an epic is created in Jira, a manual correction must be done. See this job aid for more details: fancy.nwie.net/CorrectingJiraEpicsJobAid
- Epics should NOT be deleted in E1 after they have synced to Jira
  - If the Epic was created in error or is not needed, change the status in E1 to **Cancelled** and then **archive** the Epic in Jira
- Epics can be copied to other work items in E1, but should NOT be moved
  - Copy and delete is the appropriate alternative, do not Cut/Paste
- Issues linked to an E1 Epic will be included in the progress summary
  - Includes Bug, Task, Tech Debt, Risk, and Story issue types, but NOT sub-tasks
  - Issues with a resolution of **Won't Do**, **Duplicate**, **Cannot Reproduce**, or **Not a Defect** will be excluded from the progress summary

Agile Costing: What is agile costing?

"Agile costing allows organizations to track the work being done by Agile teams and use that data to automatically create timesheet entries for financial planning… all without requiring team members to manually fill out timesheets…"

planview®
customer success center


Agile Costing: Why use Agile costing for time reporting?

1. Plan and track effort the way work is actually delivered – as a team

2. A shared source of truth determines actuals, not subjective memory or perceptions

3. Actuals are automated from existing activities, not a separate task required for associates

Agile Costing: Integration overview

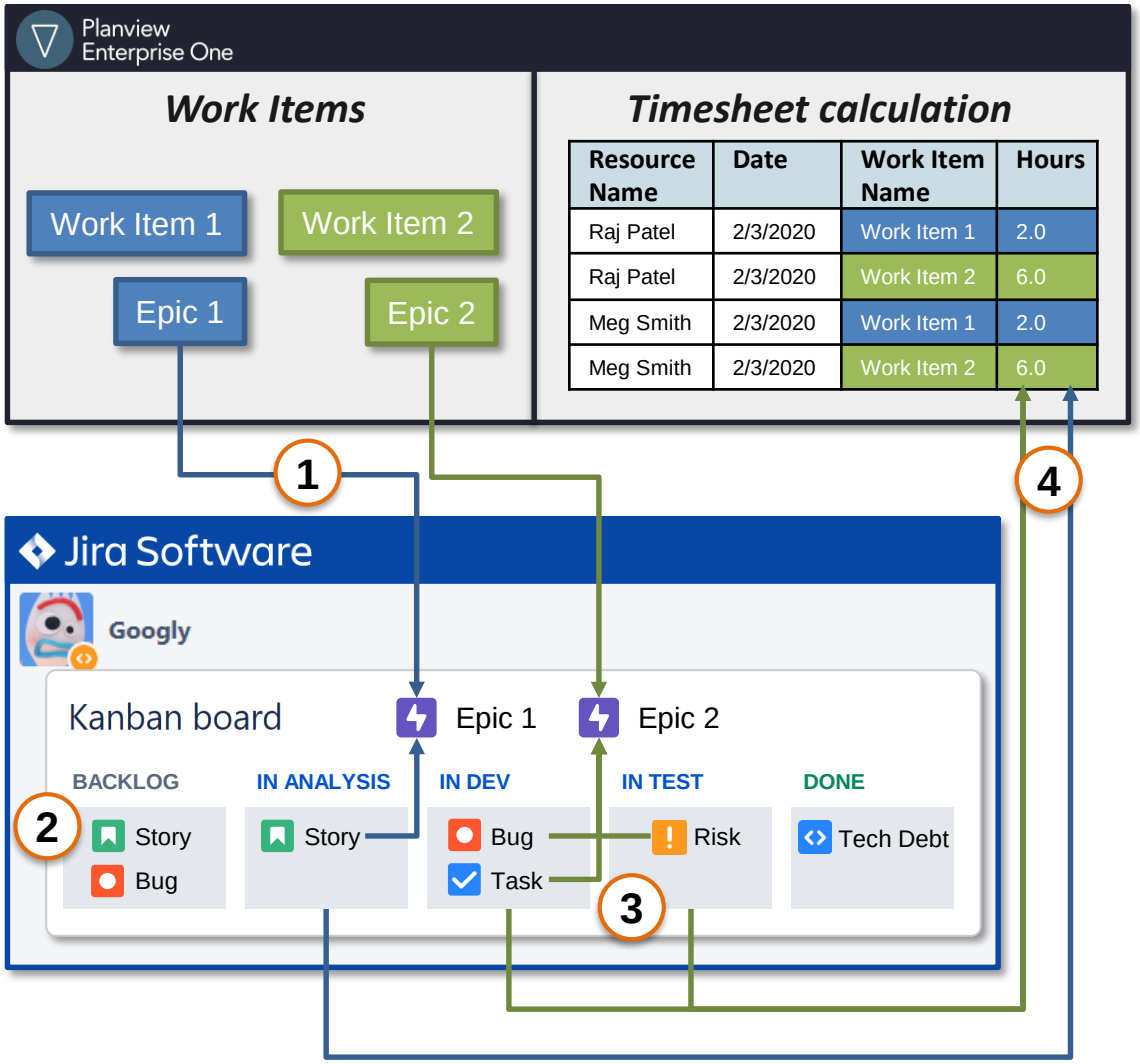

1. Epics must be created in Planview E1 and synced with Jira
2. Story, Bug, Task, Tech Debt, and Risk issues are tracked through the team's Jira workflow using Jira's virtual board
3. For a Jira issue to be considered in Agile Costing, it must be linked to an Epic that has synced from Planview E1
4. A team's Jira issues that are in progress each day are synced to Planview E1

   A calculation is performed to determine distribution of issues across the team's Work Items. For users assigned to issues, it is across their issues. For unassigned team members, it is across all the team's issues. In this example:
   - **Work Item 1:** 1/4 issues = **25%**
   - **Work Item 2:** 3/4 issues = **75%**

   Timesheets are then created for every member of the team. In this example, for an unassigned team member:
   - **Work Item 1:** 25% × 8hr = **2hr**
   - **Work Item 2:** 75% × 8hr = **6hr**

Agile Costing: Which issues get counted?


Jira issues that meet the following criteria at any point during the day are considered for Agile Costing for that day:


- In Progress
- Assigned to a user listed in Whoville
- Linked to a Planview E1 epic

Using these issues, Agile Costing will:


- Create a timesheet for everyone on the team based on the team's work
- Weight their timesheet accordingly
  - Team members who are assigned to issues will have their time spread across their work
  - Those not assigned to issues will have their time spread evenly across all work for the team

Agile Costing: Statuses and issue types included in Agile Costing

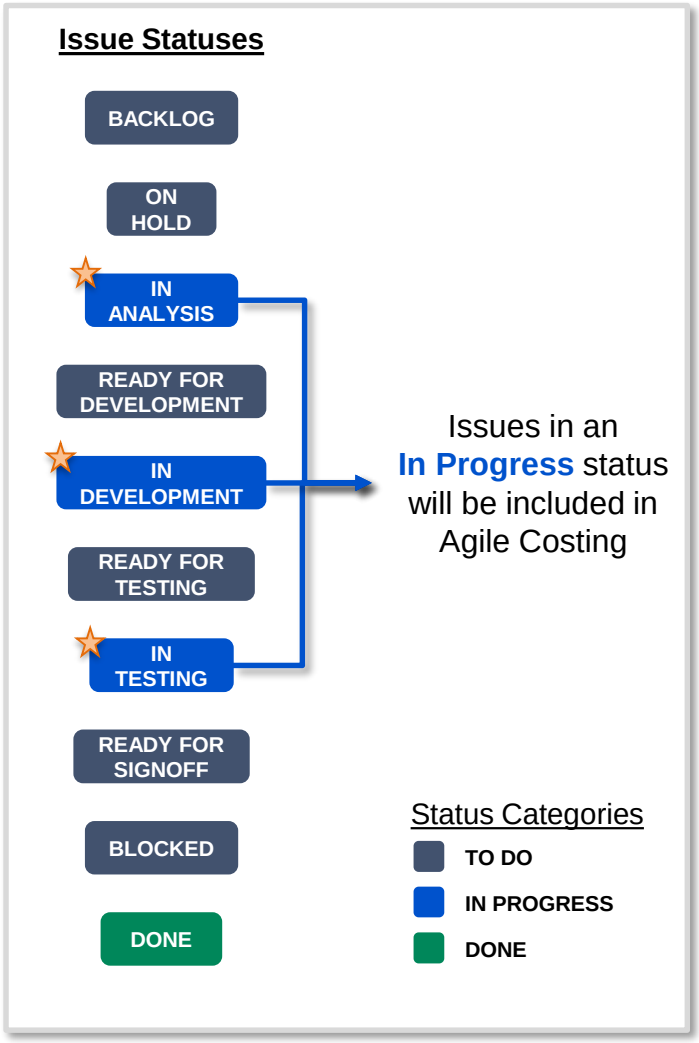

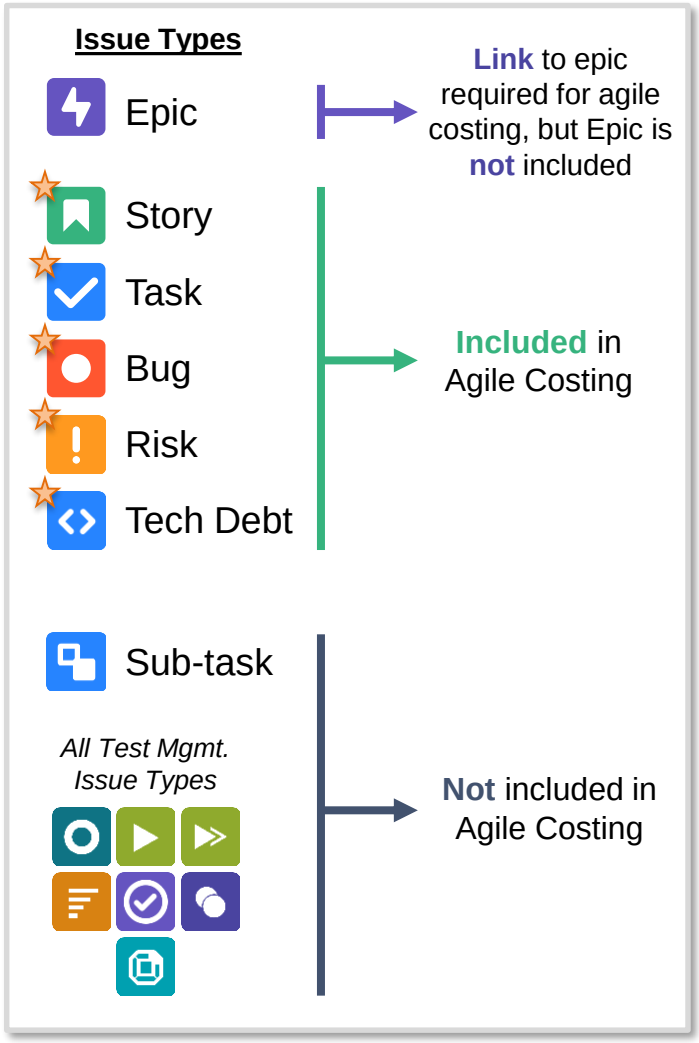


Agile Costing: Scenario 1 – One work item, one issue

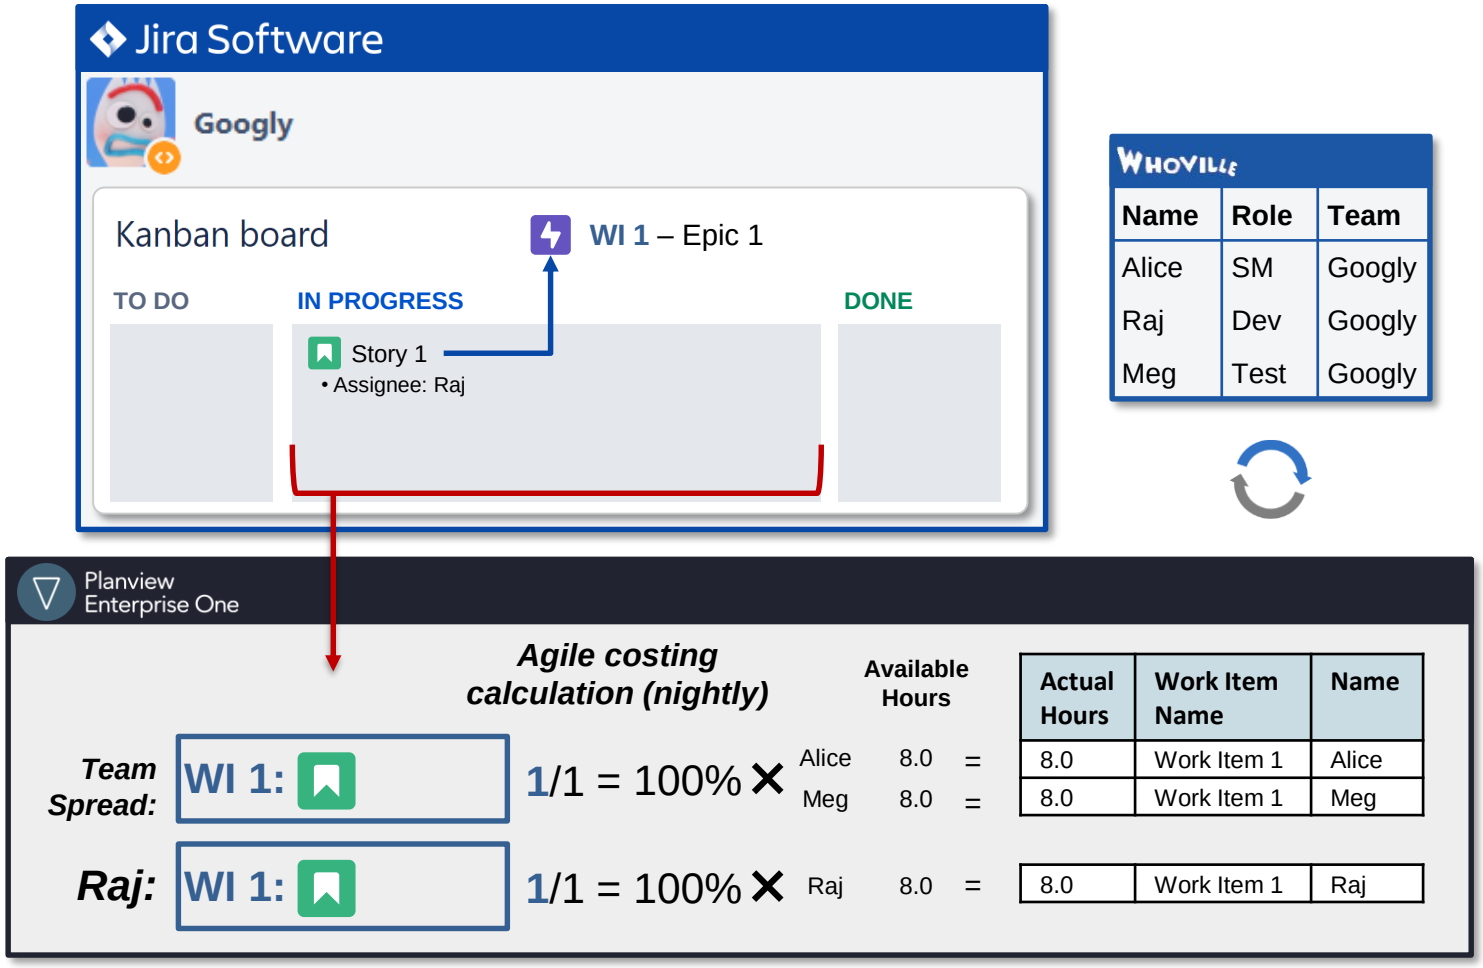


Key takeaway: Agile costing aggregates issues by Work Item

Agile Costing: Scenario 2 – Issue not assigned to team member

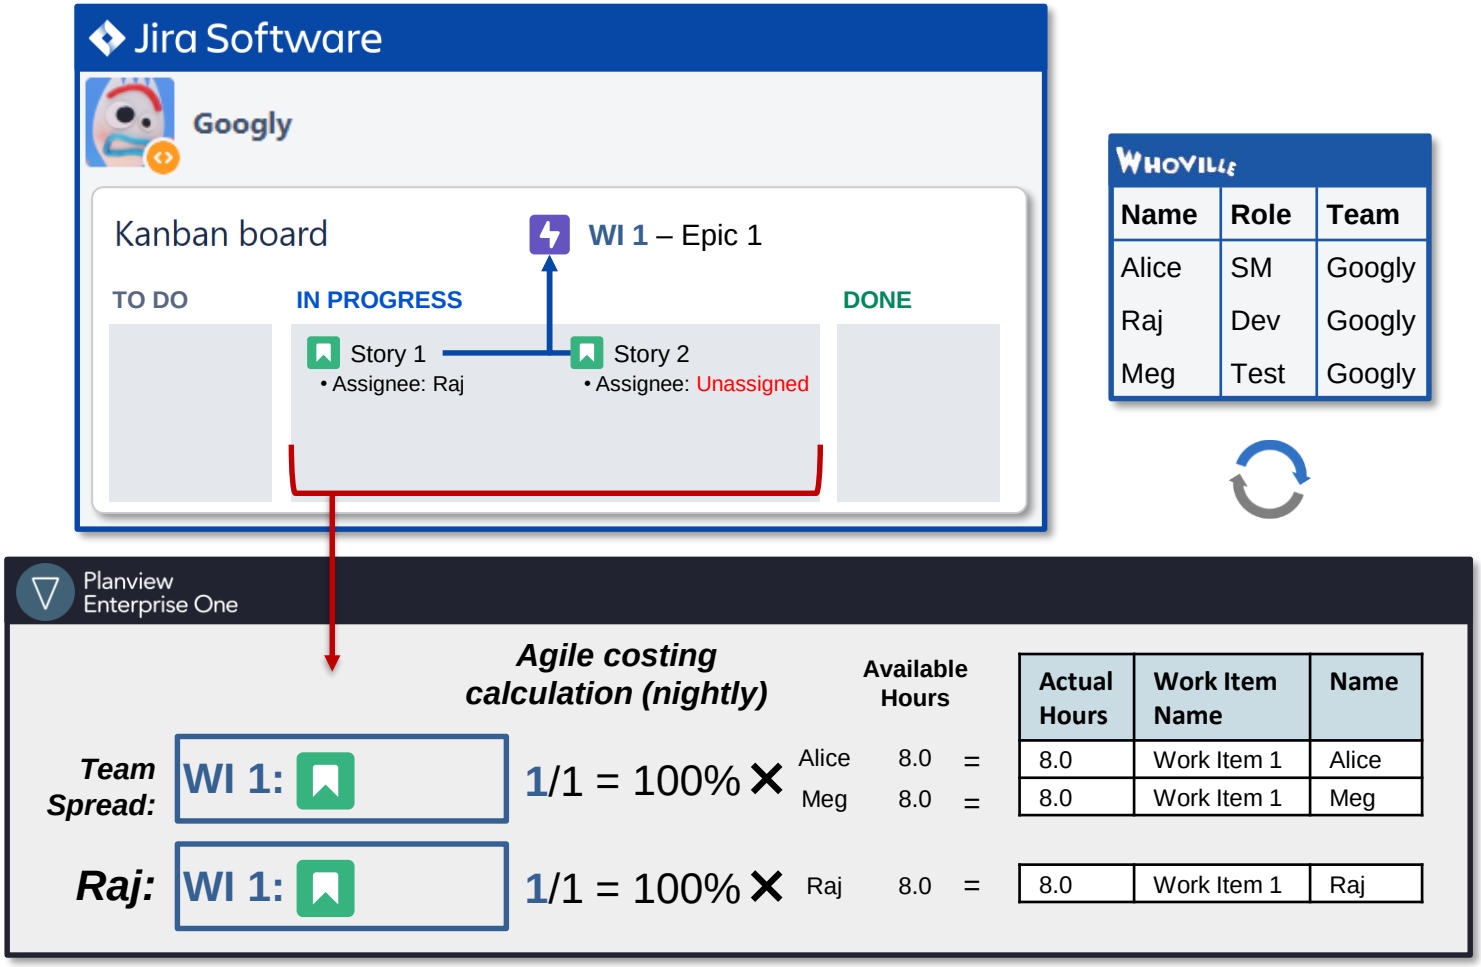


Key takeaway: Issues must be assigned to be considered for Agile Costing

Agile Costing: Scenario 3 – To Do and Done status

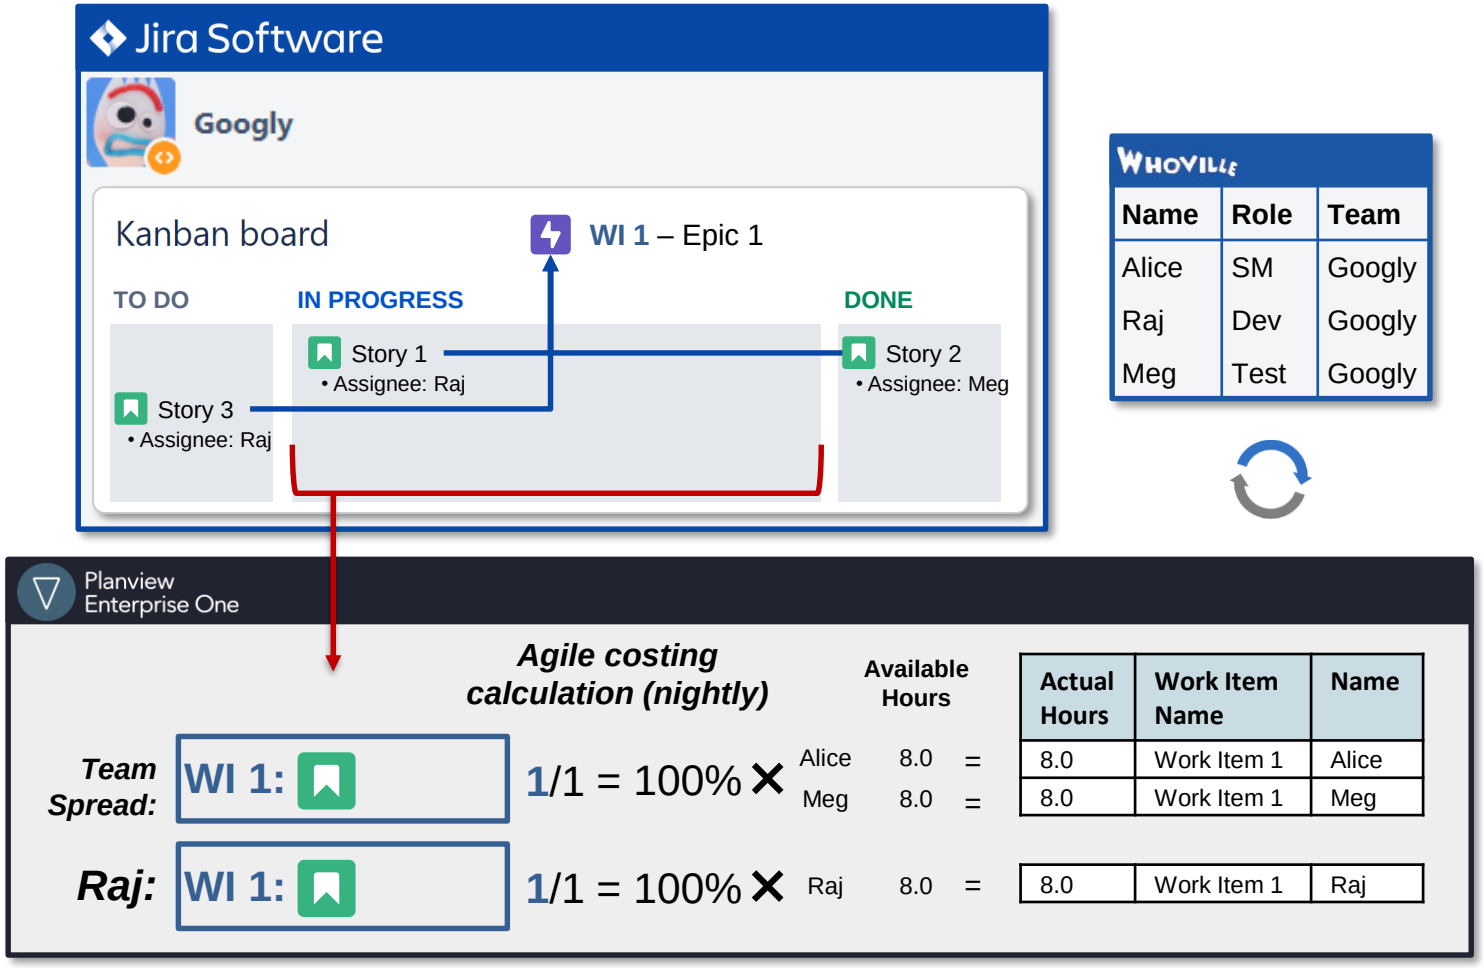


Key takeaway: Issues in To Do or Done statuses are ignored

Agile Costing: Scenario 4 – No epic link on issue

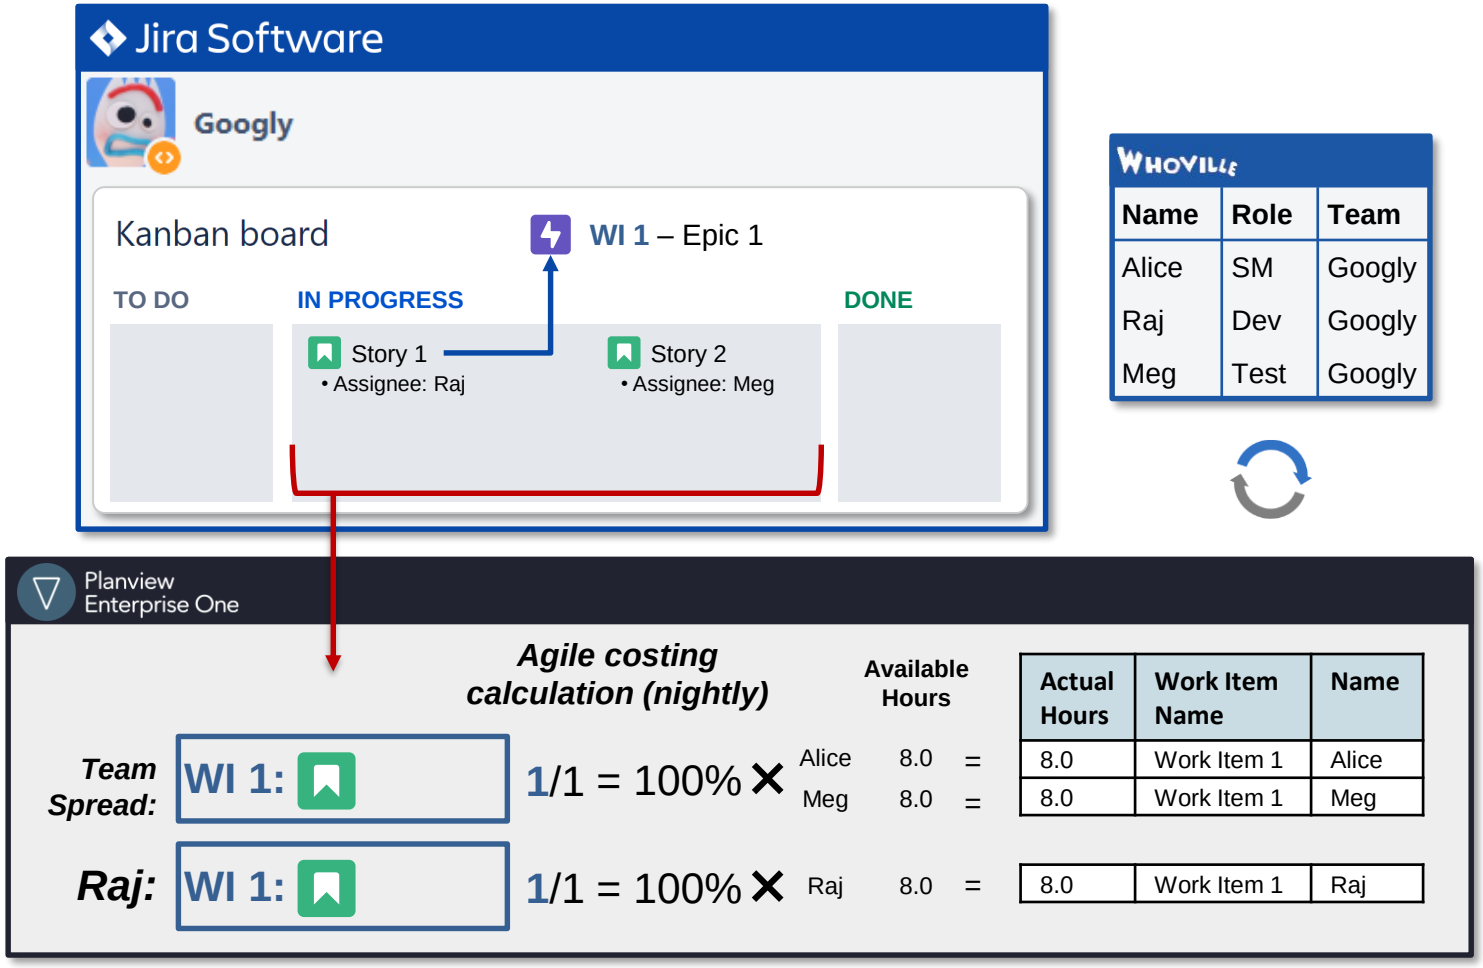


Key takeaway: Issues without an Epic link are ignored

Agile Costing: Scenario 5 – Issue put in progress mid-day

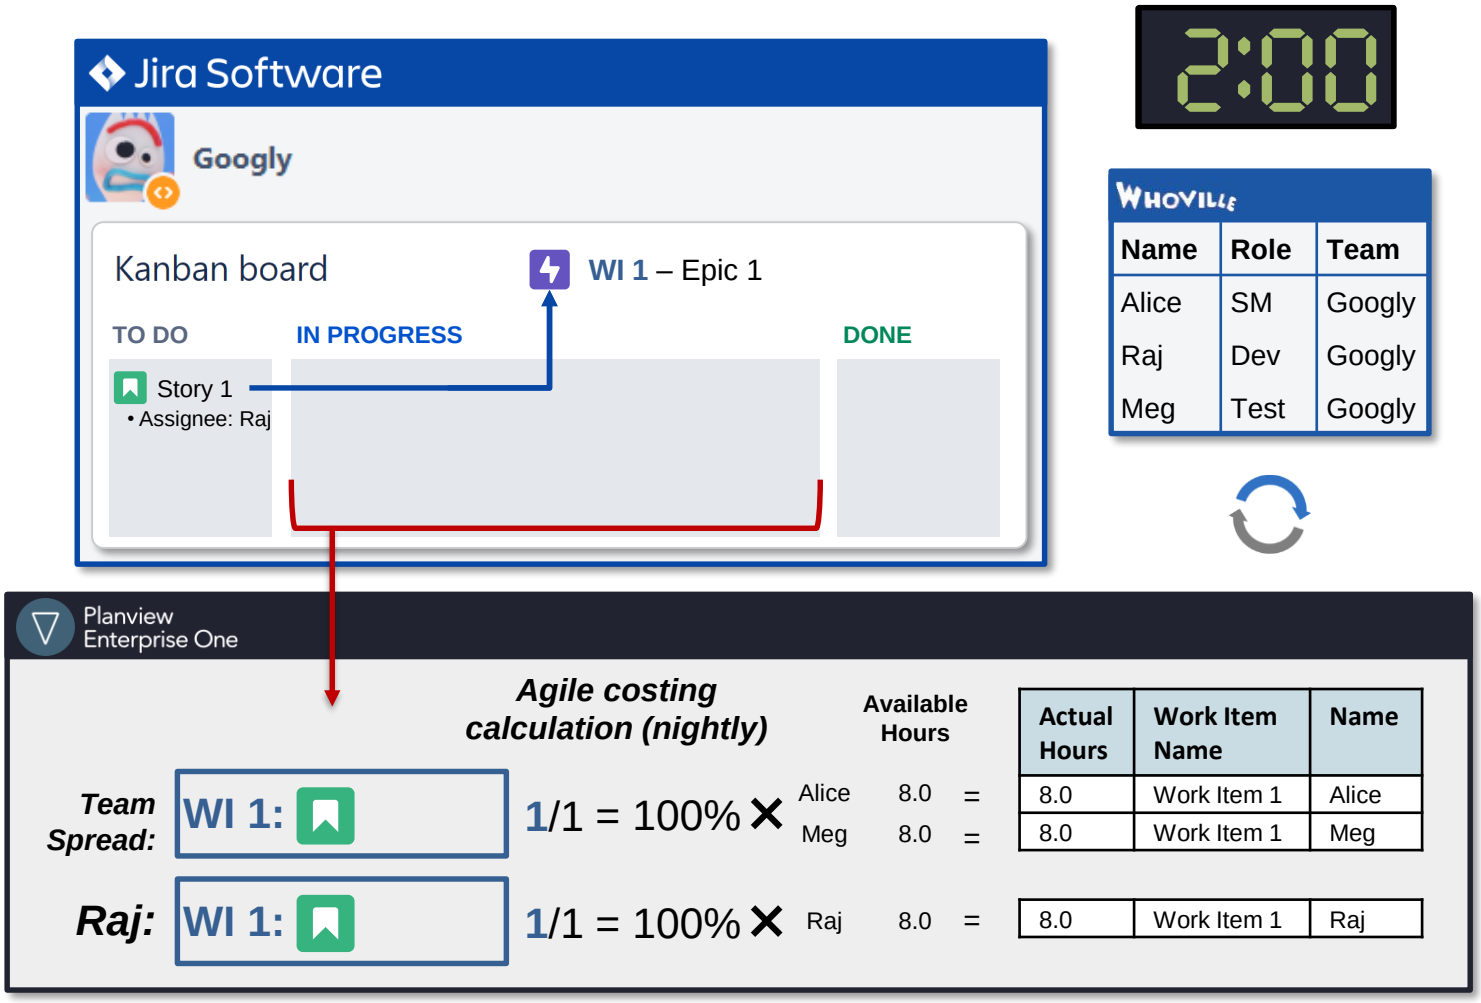


Key takeaway: Issues that spend any part of the day In Progress are included in Agile Costing

Agile Costing: Scenario 6 – Issue is assigned mid-day

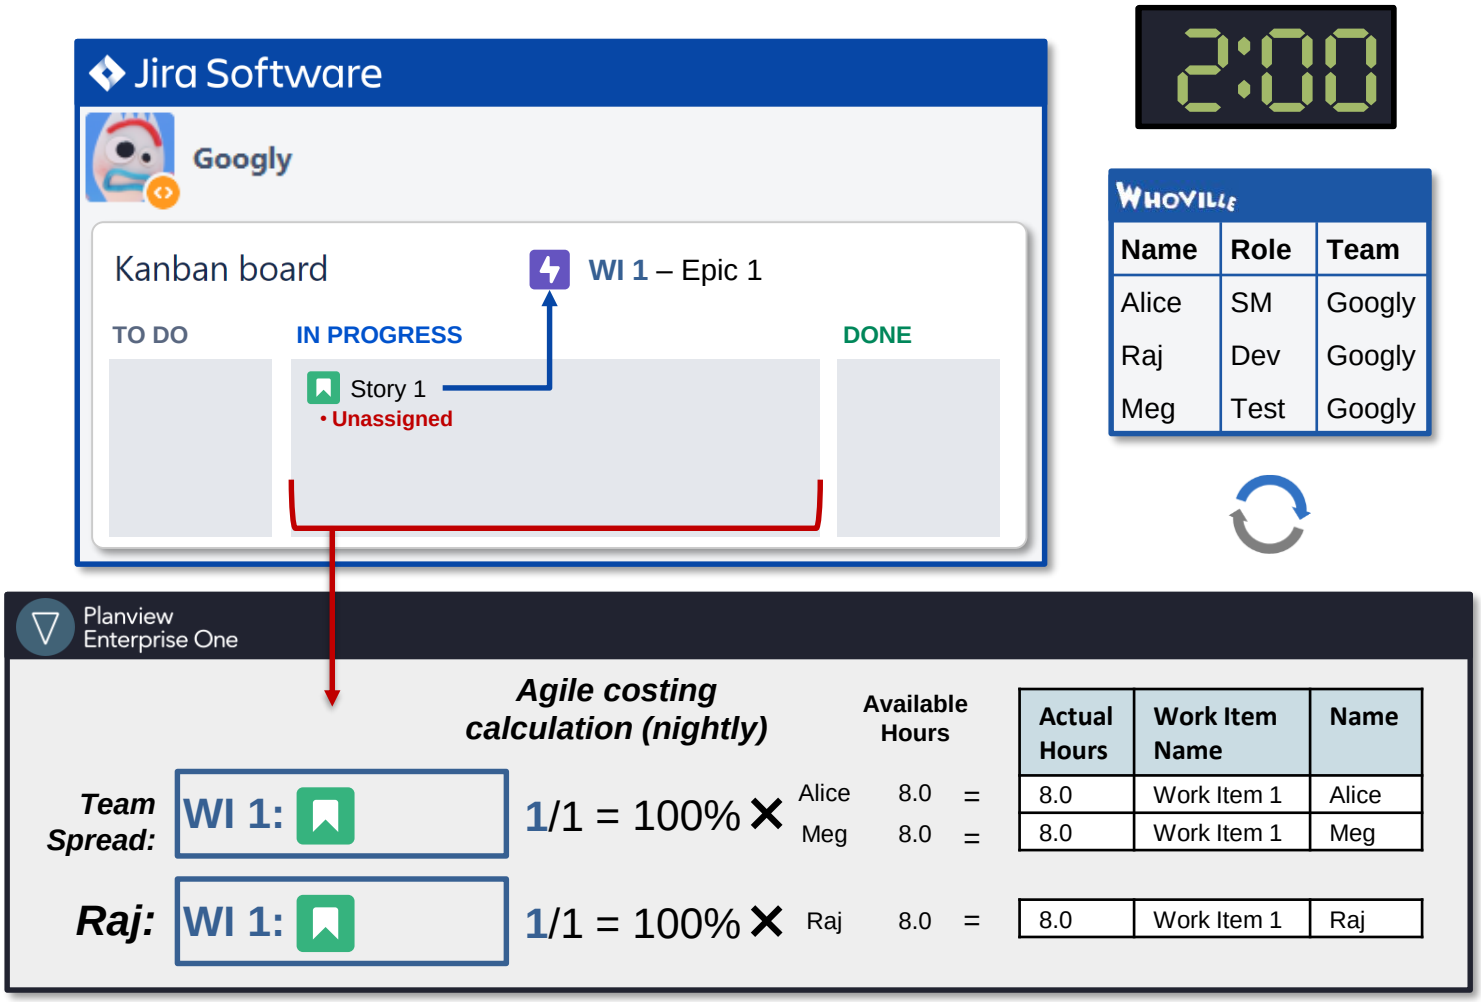


Key takeaway: Issues assigned, in progress, and linked to an epic at any time during the day will be counted

Agile Costing: Scenario 7 – Team member assigned to issue in another Jira project

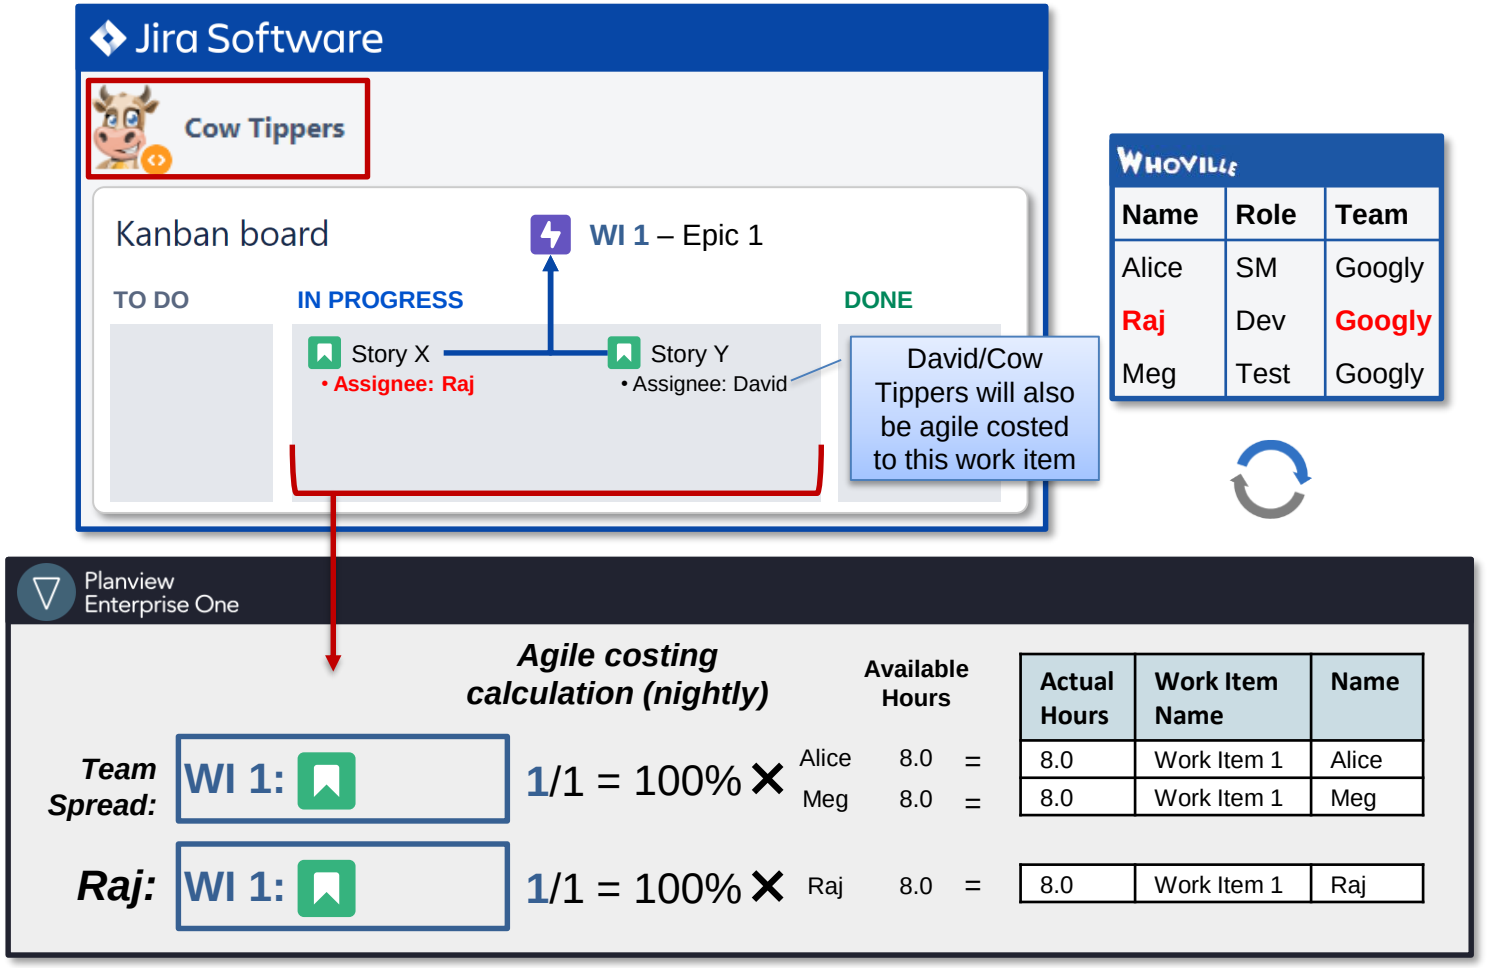

Key takeaway: Teams are determined by looking up the assignee in Whoville, not by the issue's Jira project


Agile Costing: Scenario 8 – Multiple issues, same work item

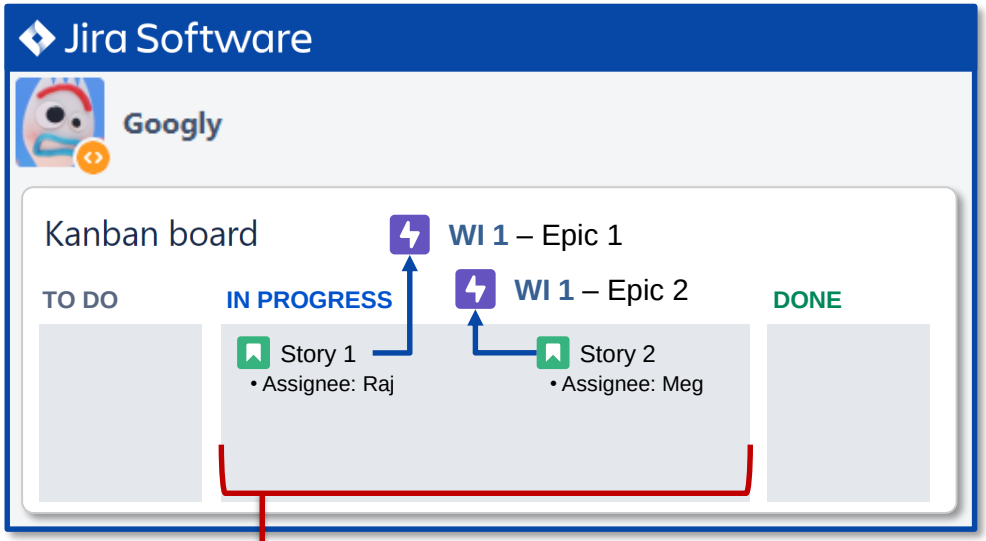

Whoville

Name	Role	Team
Alice	SM	Googly
Raj	Dev	Googly
Meg	Test	Googly




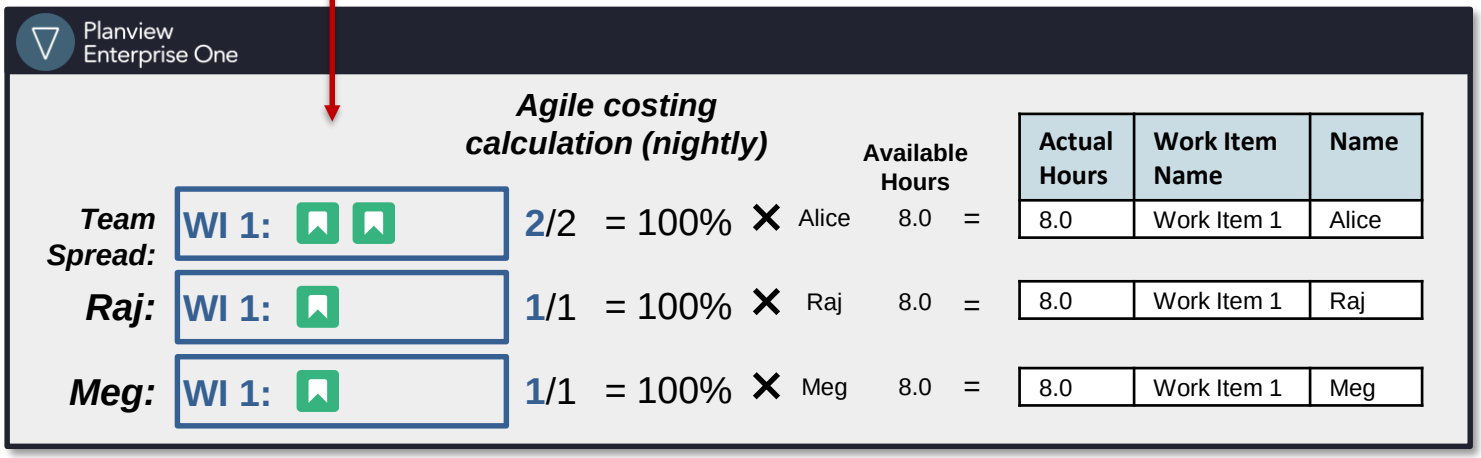

Actual Hours	Work Item Name	Name
8.0	Work Item 1	Alice
8.0	Work Item 1	Raj
8.0	Work Item 1	Meg

Key takeaway: Epics from the same Work Item are considered identically in Agile Costing

Agile Costing: Scenario 9 – Multiple work items

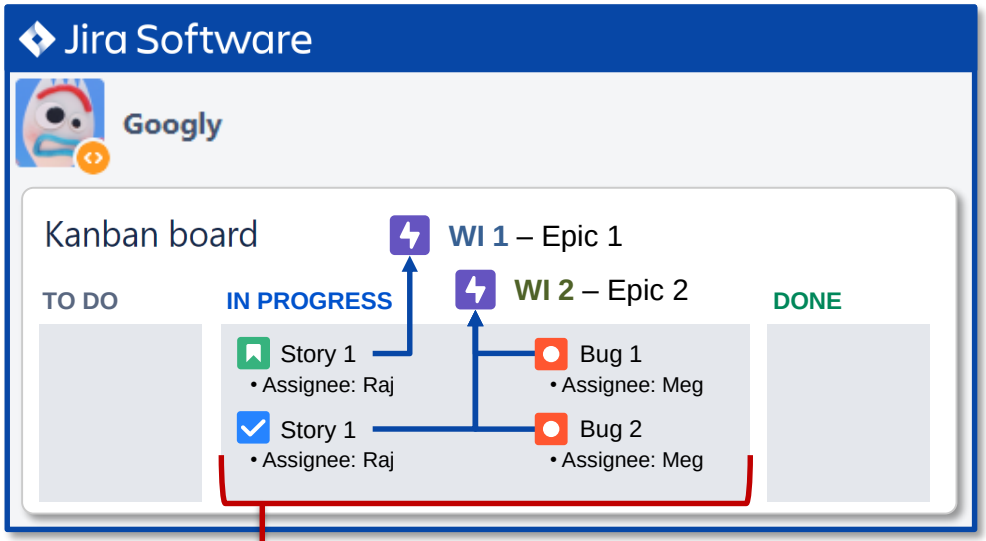

Whoville

Name	Role	Team
Alice	SM	Googly
Raj	Dev	Googly
Meg	Test	Googly




Planview Enterprise One

Agile costing calculation (nightly)

						Available Hours		Actual Hours	Work Item Name	Name
Team Spread:	WI 1:	1/4	= 25%	×	Alice	8.0	=	2.0	Work Item 1	Alice
	WI 2:	3/4	= 75%	×	Alice	8.0	=	6.0	Work Item 2	Alice
Raj:	WI 1:	1/2	= 50%	×	Raj	8.0	=	4.0	Work Item 1	Raj
	WI 2:	1/2	= 50%	×	Raj	8.0	=	4.0	Work Item 2	Raj
Meg:	WI 1:	0/2	= 0%	×	Meg	8.0	=	*No timesheet entry for WI 1*		
	WI 2:	2/2	= 100%	×	Meg	8.0	=	8.0	Work Item 2	Meg

Key takeaway: Work items are charged in proportion to their share of issues by count

Agile Costing: Scenario 10 – Time off

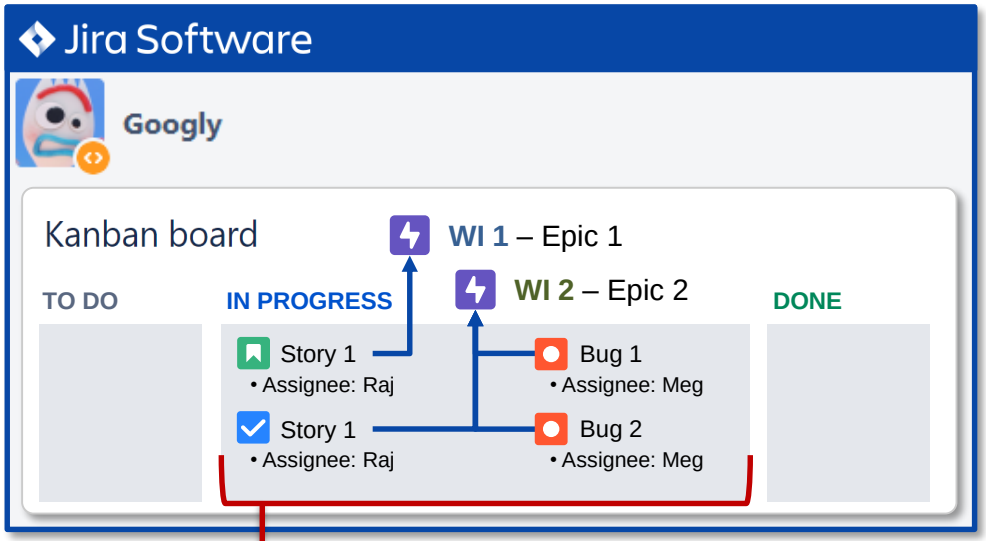

Whoville

Name	Role	Team
Alice	SM	Googly
Raj	Dev	Googly
Meg	Test	Googly

← **Full day off**

Planview Enterprise One

Agile costing calculation (nightly)

					Available Hours		Actual Hours	Work Item Name	Name
Team Spread:	WI 1:	1/4	= 25%	×	Alice	8.0 =	2.0	Work Item 1	Alice
	WI 2:	3/4	= 75%	×	Alice	8.0 =	6.0	Work Item 2	Alice
Raj:	WI 1:	1/2	= 50%	×	Raj	**0.0** =	**0.0**	Work Item 1	Raj
	WI 2:	1/2	= 50%	×	Raj	**0.0** =	**0.0**	Work Item 2	Raj
Meg:	WI 1:	0/2	= 0%	×	Meg	8.0 =	*No timesheet entry for WI 1*		
	WI 2:	2/2	= 100%	×	Meg	8.0 =	8.0	Work Item 2	Meg

Key takeaway: Timesheets are created using the available hours of each team member

Agile Costing: Helpful Tips

- Three criteria must be met for a Jira issue to be included in agile costing:
  1. Assigned to a user listed as primary for team in Whoville (can't be unassigned)
  2. In Progress status (In Analysis, In Development, In Testing)
  3. Linked to a Planview E1 epic
- Update issues every 2 weeks – Issues with no activity for 15 days will be excluded from agile costing until the next update
- When team members onboard, ensure they are unassigned from previous issues
- To remove an Epic from Agile costing, unlink the issues from the Epic, archive the Epic in Jira, and cancel the epic in E1
- Use the Standard Weekly Checklists which can be found on the Planview E1 Education Hub
- If you need to exclude a single person or an entire team from agile costing, you can do so by unchecking the "agile costing" field in Whoville on the team or person record.

Agile Costing: FAQs

Should I create separate issues to represent Requirements Analysis work?

- Not typically. Create story issues, assign the RA, and move them into In Analysis when decomposition work is occurring

Should I create issues for each incident I work?

- No. Incident resolution work should be managed in Service Now and an allocation should be added to those work items for that effort. Incident action items may become Jira issues

How long does an issue need to be In Progress to be counted in agile costing?

- Ideally, issues in progress longer than 5 minutes will be included in agile costing. At times, the sync to the agile costing engine can lag, in which case issues may need to be in progress for up to a few hours to be included

How many hours does Agile Costing charge per card?

- This is a common misconception. Agile costing does not equate hours to cards. It uses the distribution of active cards to work items
- In other words, agile costing calculates what percentage of the total pie each work item gets, not how big the pie is

Can I see what issues were included for my team in Agile Costing?

- Not at this time, but this is an enhancement idea we have submitted to Planview

Training, resources, and communication channels

Jira Education Hub

Planview E1 Education Hub

Set up a consultation session on the Planview E1 Education Hub


Teaching Thursday class offerings

JiraBot self-service chatbot assistant

Rocket Chat: #jira #planview_scrummaster_champions

Appendix

Work Traceability: Epic name sync behavior

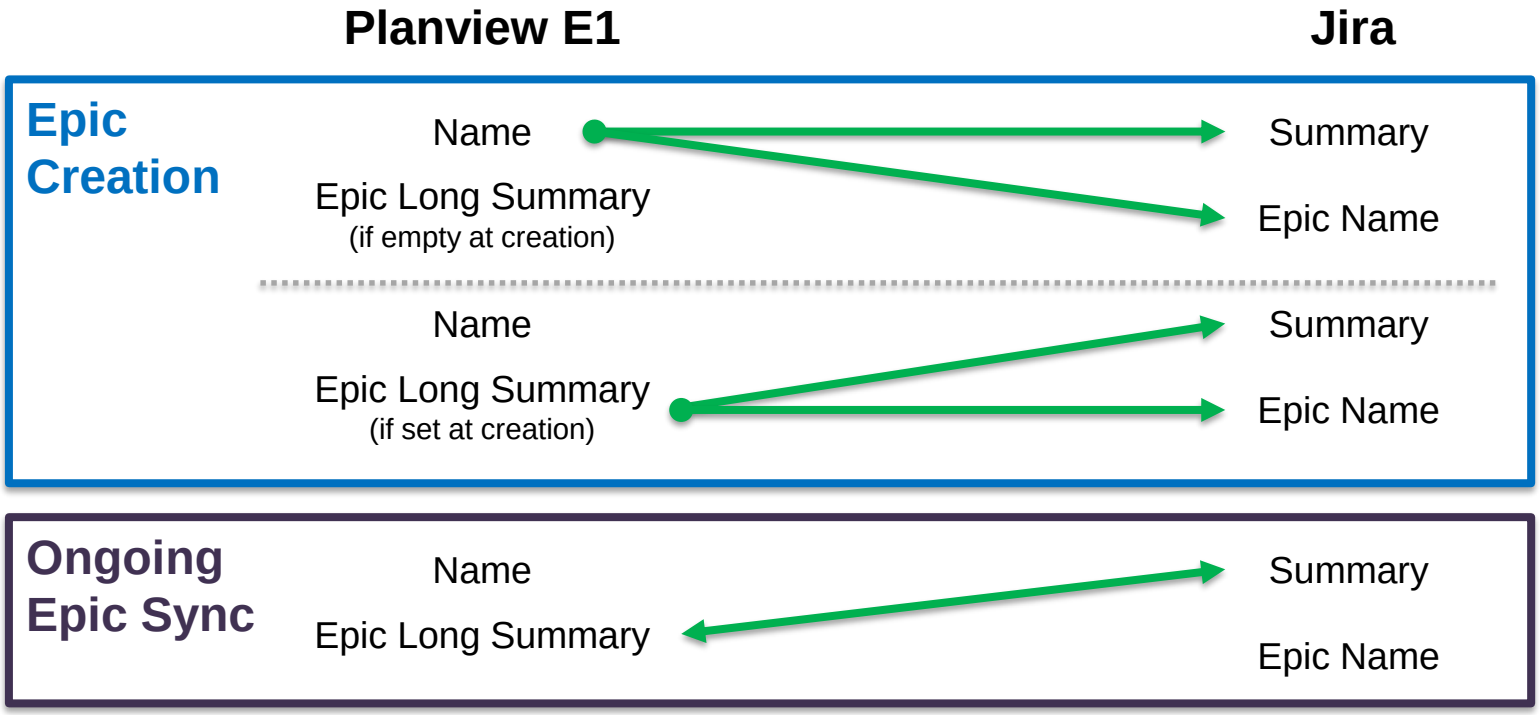

Detailed fields included in Epic Sync

Planview E1	Jira	Comments
Sync with Jira (Yes/No)	N/A	Must be Yes for epic to sync
Team Alignment (Jira Project)	Jira Project Name	Must be filled out for epic to sync. After set, should only be updated in Jira
Name	Summary	Name field is limited to 50 characters. Name field syncs at creation – Epic Long Summary kept updated
Epic Long Summary		
Work ID	Planview Work Item ID	Read only in Jira
Work Name	Planview Work Item Name	Read only in Jira
Work Type (Build/Run)	Planview Work Type	Read only in Jira
Card Count	Card Count	Calculated in Jira, synced to E1
Number Completed Cards	Number Completed Cards	Calculated in Jira, synced to E1
Total Epic Points	Total Epic Points	Calculated in Jira, synced to E1
Total Completed Epic Points	Total Completed Epic Points	Calculated in Jira, synced to E1
Hyperlink to Epic	Links To	Hyperlink to E1 from Jira
Jira Issue Key	Issue Key	Jira Key / hyperlink to Jira from E1
